

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1		32%		1	BID 2546/OC-DR Programa de Apoyo al Sistema Nacional de Empleo (PASNE)	1356 days	30 Jan '12	12 Apr '17
2		37%		1.1	Componente 1: Apoyo a servicios de intermediación	1303.2 day	30 Jan '12	30 Jan '17
3		19%		1.1.1	Sub -Componente 1.1: Fortalecimiento Dirección C	1303.2 day	30 Jan '12	30 Jan '17
4		100%		1.1.1.1	Producto 1: Dirección General de Empleo (DGE)	1154 days	30 Jan '12	30 Jun '16
6		100%		1.1.1.2	Producto 2: Sistema informático de gestión del S	1154 days	30 Jan '12	30 Jun '16
8		100%		1.1.1.3	Producto 3: Sistema Integrado de Capacitación I	1154 days	30 Jan '12	30 Jun '16
10		100%		1.1.1.4	Producto 4: Portal de Empleo implementado	1154 days	30 Jan '12	30 Jun '16
12		100%		1.1.1.5	Producto 5: Sistema de calidad en normas ISO 9	1154 days	30 Jan '12	30 Jun '16
14		100%		1.1.1.6	Producto 6: Instrumento de focalización (índice	1154 days	30 Jan '12	30 Jun '16
16		4%		1.1.1.7	Producto 7: Personal del SENAE capacitado	1293 days	30 Jan '12	13 Jan '17
17		100%		1.1.1.7.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
18		0%		1.1.1.7.2	Plan de Actividades Agosto - Diciembre 2017	1258 days	30 Jan '12	24 Nov '16
19		0%		1.1.1.7.2	Recepción de requerimiento	1 day	25 Aug '16	25 Aug '16
20		0%		1.1.1.7.2	Estructuración del Plan de Actividades	2 days	26 Aug '16	29 Aug '16
21		0%		1.1.1.7.2	Elaboración solicitud de no objeción al Banco	2 days	30 Aug '16	31 Aug '16
22		0%		1.1.1.7.2	Remisión de Solicitud de no objeción al Banco	2 days	01 Sep '16	02 Sep '16
23		0%		1.1.1.7.2	Recepción de No Objeción del Banco	5 days	05 Sep '16	09 Sep '16
24		0%		1.1.1.7.2	Contratación de facilitadores	65.5 days	12 Aug '16	14 Nov '16
76		0%	CP-SD-PC/01-20	1.1.1.7.2	CP-SD-PC/01-2016 - Alimentación para Jorn	1214.5 day	30 Jan '12	26 Sep '16
92		0%	CP-B-PC/01-201	1.1.1.7.2	CP-B-PC/01-2016 - Material Gastable	31.5 days	12 Aug '16	27 Sep '16

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
106		0%	CP-SD-PC/02-20	1.1.1.7.2	CP-SD-PC/02-2016 - Impresión y Reproduc	31.5 days	12 Aug '16	27 Sep '16
120		0%	CP-SD-PC/03-20	1.1.1.7.2	CP-SD-PC/03-2016 - Locación y alimentaci	74 days	12 Aug '16	24 Nov '16
136		0%		1.1.1.7.3	Taller de capacitación a las OTEs	1213.5 day	30 Jan '12	23 Sep '16
137		0%		1.1.1.7.3	Taller OTE's en Hotel (2 días) Juan Dolio	1213.5 day	30 Jan '12	23 Sep '16
144		0%	CCI-04/2016	1.1.1.7.3	CCI-04/2016 - Contratación de facilitador	27.5 days	09-Sep-'16	19-Oct-'16
149		0%	CP-SD-PC/01-20	1.1.1.7.3	CP-SD-PC/01-2016 - Alimentación	17 days	19-Sep-'16	12-Oct-'16
156		0%	CP-B-PC/01-201	1.1.1.7.3	CP-B-PC/01-2016 - Material Gastable	26.5 days	09-Sep-'16	18-Oct-'16
161		0%	CP-SD-PC/02-20	1.1.1.7.3	CP-SD-PC/02-2016 - Impresión y reproduc	26.5 days	09-Sep-'16	18-Oct-'16
165		48%	CD-SD-01/2016	1.1.1.7.4	CD-SD-01/2016 - Diplomado en metodologia d	139 days	01 Jul '16	13 Jan '17
174		100%		1.1.1.8	Producto 8: Evento Internacional sobre los Servi	1154 days	30 Jan '12	30 Jun '16
176		100%		1.1.1.9	Producto 9: OTE Supervisadas	1154 days	30 Jan '12	30 Jun '16
178		38%		1.1.1.10	Producto 10: Oficinas Territoriales de Empleo (O	1303.2 day	30 Jan '12	30 Jan '17
179		100%		1.1.1.10	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
180		0%		1.1.1.10	1693 OC-DR: Adquisición de equipos de comer	30 days	17 Aug '16	27 Sep '16
181		0%		1.1.1.10	Aprobación del Ministro	15 days	17 Aug '16	06 Sep '16
182		0%		1.1.1.10	Pago deuda pendiente y aprobada mediante	15 days	07 Sep '16	27 Sep '16
183		34%		1.1.1.10	Unidad Móvil	158.5 days	19 Apr '16	28 Nov '16
184		58%	LPN-B-02/2016	1.1.1.10	LPN-B-02/2016 - Adquisición de Unidad Móv	158 days	19 Apr '16	25 Nov '16
203		0%	CP-B-06/2016	1.1.1.10	CP-B-06/2016 - Adquisición de mobiliario pa	52.5 days	06 Sep '16	17 Nov '16
221		0%	CP-B-07/2016	1.1.1.10	CP-B-07/2016 - Adquisición de equipos infor	59.5 days	06 Sep '16	28 Nov '16
239		58%	CP-B-01/2016	1.1.1.10	CP-B-01/2016 - Adquisición de equipos inform	231.5 days	07 Jan '16	28 Nov '16

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
271		70%	CP-B-02/2016	1.1.1.10	CP-B-02/2016 - Adquisición de mobiliario ***	242.5 days	07 Jan '16	13 Dec '16
303		10%	LPN-B-03/2016	1.1.1.10	LPN-B-03/2016 - Adquisición de equipos inform	109.2 days	29 Aug '16	30 Jan '17
329		0%	CP-B-08/2016	1.1.1.10	CP-B-08/2016 - Adquisición de mobiliario ***	99.5 days	29 Aug '16	16 Jan '17
361		10%	CP-B-09/2016	1.1.1.10	CP-B-09/2016 - Adquisición de acondicionador	45.5 days	05 Aug '16	10 Oct '16
384		0%		1.1.1.10	Adquisición de UPS-Banco de Baterías para las	15 days	17 Aug '16	06 Sep '16
385		0%		1.1.1.10	Pago de deuda de Instalación de UPS-Banco (15 days	17 Aug '16	06 Sep '16
386		100%		1.1.1.11	Producto11: Personal para atender vía call cente	1154 days	30 Jan '12	30 Jun '16
388		8%		1.1.1.12	Producto 12: Personal nuevo para el SENA rem	1271 days	30 Jan '12	13 Dec '16
389		100%		1.1.1.12	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
390		8%	CD-SD-02/2016	1.1.1.12	CD-SD-02/2016 - Pasantía de 20 personas en 1	107 days	15 Jul '16	13 Dec '16
403		100%		1.1.1.13	Producto 13: Personal para el funcionamiento d	1154 days	30 Jan '12	30 Jun '16
405		100%		1.1.1.14	Producto 14: Integración del SENA con Asociaci	1222 days	30 Jan '12	05 Oct '16
406		100%		1.1.1.14	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
407		100%		1.1.1.14	Afiliación a la AMSPE	22 days	06 Sep '16	05 Oct '16
411		100%		1.1.1.15	Producto 15: Personal de la Unidad de Capacitación del SENA remunerado y operando	1154 days	30 Jan '12	30 Jun '16
413		11%		1.1.2	Sub-componente 1.2: Promoción de Empleo	1283 days	30 Jan '12	29 Dec '16
414		36%		1.1.2.1	Producto 16: Encuentros Empresariales realizad	1273 days	30 Jan '12	15 Dec '16
415		100%		1.1.2.1.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
416		36%		1.1.2.1.2	Encuentros Empresariales (2)	101 days	27 Jul '16	15 Dec '16
417		0%	CP-SD-PC/03-20	1.1.2.1.2	CP-SD-PC-04/2016 - Servicio de Alimentación	86 days	17 Aug '16	15 Dec '16

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
422		81%	CP-B-11/2016	1.1.2.1.1	CP-B-011/2016 - Material gastable para Encu	31 days	27 Jul '16	08 Sep '16
428		94%	CP-SD-14/2016	1.1.2.1.2	CP-SD-14/2016 - Impresos para encuentros	31 days	27 Jul '16	08 Sep '16
434		0%	CP-SD-PC/03-20	1.1.2.1.3	CP-SD-PC-03/2016 - Servicio de Alimentación	86 days	17 Aug '16	15 Dec '16
439		0%		1.1.2.2	Producto 17: Estrategia de Comunicación para e	1259.5 day	30 Jan '12	28 Nov '16
440		100%		1.1.2.2.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
441		0%		1.1.2.2.2	1693 OC-DR: Publicidad OTE - SENAE vía emiso	30 days	17 Aug '16	27 Sep '16
442		0%		1.1.2.2.2	Aprobación del Ministro	15 days	17 Aug '16	06 Sep '16
443		0%		1.1.2.2.2	Pago deuda pendiente y aprobada mediante	15 days	07 Sep '16	27 Sep '16
444		0%		1.1.2.2.3	Estrategia de Comunicación del SENAE	65.5 days	29 Aug '16	28 Nov '16
445		0%	CP-SD-05/2016	1.1.2.2.3	CP-SD-05/2016 - Impresión de Guías, Brochu	65.5 days	29 Aug '16	28 Nov '16
468		100%		1.1.2.3	Producto 18: Materiales Capacitación realizados	1154 days	30 Jan '12	30 Jun '16
469		100%		1.1.2.3.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
470		0%	CP-SD-05/2016	1.1.2.3.2	CP-SD-05/2016: Impresión de guía de búsqued	27 days	27 Oct '16	05 Dec '16
474		0%		1.1.2.4	Producto 19: Jornadas de promoción de empleo	1283 days	30 Jan '12	29 Dec '16
475		100%		1.1.2.4.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
476		0%		1.1.2.4.2	Jornadas de Promoción de Empleo	79 days	12 Sep '16	29 Dec '16
477		0%	CP-SD-PC/01-20	1.1.2.4.2	CP-SD-PC/01-2016 - Servicio de Alimentación	79 days	12 Sep '16	29 Dec '16
495		0%		1.1.2.4.2	Pago de viáticos:	55 days	21 Sep '16	06 Dec '16
503		0%	CP-SD-PC/01-20	1.1.2.4.2	CP-SD-PC/01-2016 - Carpas y Sillas:	70 days	21 Sep '16	27 Dec '16
521		22%		1.1.3	Sub-Componente 1.3: Intermediación Laboral	1283 days	30 Jan '12	29 Dec '16
522		100%		1.1.3.1	Producto 20: Kioscos de Empleo operando	1154 days	30 Jan '12	30 Jun '16

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
524		44%		1.1.3.2	Producto 21: Jornadas de Empleo realizadas	1278 days	30 Jan '12	22 Dec '16
525		100%		1.1.3.2.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
526		0%		1.1.3.2.2	1693 OC-DR: Publicidad OTE - SENA E vía emis	30 days	17 Aug '16	27 Sep '16
527		0%		1.1.3.2.2	Aprobación del Ministro	15 days	17 Aug '16	06 Sep '16
528		0%		1.1.3.2.2	Pago deuda pendiente y aprobada mediante	15 days	07 Sep '16	27 Sep '16
529		44%		1.1.3.2.3	Jornadas de empleo (5)	215 days	24 Feb '16	22 Dec '16
530		50%	CP-SD-PC/01-20	1.1.3.2.3	CP-SD-PC/01-2016 - Servicio de Alimentación	215 days	24 Feb '16	22 Dec '16
544		88%		1.1.3.2.3	Pago de viáticos:	199 days	24 Feb '16	30 Nov '16
550		0%	CP-SD-PC/01-20	1.1.3.2.3	CP-SD-PC/01-2016 - Carpas y Sillas:	215 days	24 Feb '16	22 Dec '16
564		6%		1.1.3.3	Producto 22: Personas atendidas en talleres de orientación ocupacional	1283 days	30 Jan '12	29 Dec '16
565		100%		1.1.3.3.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
566		6%		1.1.3.3.2	20 Talleres para jóvenes de orientación ocupa	1283 days	30 Jan '12	29 Dec '16
567		8%	CP-SD-03/2016	1.1.3.3.2	CP-SD-03-2016 - Servicio de Alimentación	1283 days	30 Jan '12	29 Dec '16
613		0%	CP-SD-PC/01-20	1.1.3.3.2	CP-SD-PC/01-2016 - Servicio de Alimentación	78 days	25 Jul '16	10 Nov '16
621		45%		1.1.4	Sub-Componente 1.4: Capacitación Laboral	1303 days	30 Jan '12	27 Jan '17
622		8%		1.1.4.1	Producto 23: Material de Apoyo para la Capacit	1262.5 day	30 Jan '12	01 Dec '16
623		100%		1.1.4.1.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
624		24%	CP-SD-04/2016	1.1.4.1.2	CP-SD-04/2016 - Impresión de Manuales de In	21 days	09 Aug '16	07 Sep '16
630		0%	CP-SD-05/2016	1.1.4.1.3	CP-SD-05/2016 - Impresión de Materiales para	20 days	03 Nov '16	01 Dec '16
646		100%		1.1.4.2	Producto 24: Jóvenes Capacitados en Desarrollo	1154 days	30 Jan '12	30 Jun '16

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
648		100%		1.1.4.3	Producto 25: Jóvenes Capacitados en Desarrollo de Competencias DCB) Básicas más	1154 days	30 Jan '12	30 Jun '16
650		13%		1.1.4.4	Producto 26: Jóvenes capacitados en Desarrollo de Competencias Básicas (DCB) + Técnico	1216 days	30 Jan '12	27 Sep '16
651		100%		1.1.4.4.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
652		0%		1.1.4.4.2	1693 OC-DR: Liquidación de cursos y estipendi	30 days	17 Aug '16	27 Sep '16
653		0%		1.1.4.4.2	Aprobación del Ministro	15 days	17 Aug '16	06 Sep '16
654		0%		1.1.4.4.2	Pago deuda pendiente y aprobada mediante	15 days	07 Sep '16	27 Sep '16
655		17%	CP-SD-06/2016	1.1.4.4.3	CP-SD-06/2016 - Adquisición seguro de accide	23 days	10 Aug '16	12 Sep '16
661		32%		1.1.4.5	Producto 27: Jóvenes capacitados en Desarrollo de Competencias Básicas (DCB) + Técnico	1303 days	30 Jan '12	27 Jan '17
662		100%		1.1.4.5.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
663		35%	SD-01/2016	1.1.4.5.2	SD-01/2016 - Curso Modalidad J & E (45 cursos	79 days	29 Aug '16	15 Dec '16
860		30%	SD-02/2016	1.1.4.5.3	SD-02/2016 - Curso Modalidad J & E (42 cursos	75 days	29 Aug '16	09 Dec '16
1053		0%		1.1.4.5.4	Supervisión de cursos y entrenamientos INFO	130 days	16 Dec '16	27 Jan '17
1056		27%		1.1.4.6	Producto 28: Personas capacitadas en Entrenam	1288 days	30 Jan '12	05 Jan '17
1057		100%		1.1.4.6.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1058		38%	SD-03/2016	1.1.4.6.2	SD-03/2016 - Cursos Modalidad EIL (700 jóven	40 days	05 Sep '16	28 Oct '16
1059		0%		1.1.4.6.2	DMG-International, INC	44 days	26-Sep-16	24 Nov '16
1063		50%		1.1.4.6.2	Hotel Jaragua	40 days	05 Sep '16	28 Oct '16
1067		0%		1.1.4.6.2	LGS-International	40 days	01-Jul-16	26-Aug-16

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1071		25%		1.1.4.6.2	Colinas Business (Paqueta)	40 days	05 Sep '16	28 Oct '16
1075		0%		1.1.4.6.3	Supervisión de cursos y entrenamientos INFO1	149 days	31 Oct '16	05 Jan '17
1078		77%		1.1.4.7	Producto 29: Jóvenes Capacitados en Programa Piloto Formación para el Autoempleo	1271 days	30 Jan '12	13 Dec '16
1079		100%		1.1.4.7.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1080		83%	SD-04/2016	1.1.4.7.2	SD-04/2016 - Contratación Cursos Modalidad (102 days	01 Jul '16	22 Nov '16
1334		0%		1.1.4.7.3	Supervisión de cursos y entrenamientos INFO1	130 days	02 Nov '16	13 Dec '16
1337		62%	CD-CCIN-01/201	1.1.4.7.4	CD-CCIN-01/2016 - Consultoría para Elaboraci	42 days	21 Jun '16	18 Aug '16
1348		27%		1.1.4.7.5	Primer taller de capacitación a profesores de e	1177 days	22 Feb '12	26 Aug '16
1349		100%		1.1.4.7.5	Ejecución del taller	3 days	23 Aug '16	25 Aug '16
1350		26%	CP-SD-07/2016	1.1.4.7.5	CP-SD-07/2016 - Servicio de Alimentación	27 days	20 Jul '16	26 Aug '16
1356		28%	CP-B-10/2016	1.1.4.7.5	CP-B-10/2016 - Material Gastable	25 days	20 Jul '16	24 Aug '16
1362		28%	CP-SD-08/2016	1.1.4.7.5	CP-SD-08/2016 - Impresión	1160 days	22 Feb '12	02 Aug '16
1368		0%		1.1.4.7.6	Segundo taller de capacitación a profesores de	40.5 days	23 Aug '16	18 Oct '16
1369		100%		1.1.4.7.6	Ejecución del taller	3 days	23 Aug '16	25 Aug '16
1370		0%	CP-SD-PC/01-20	1.1.4.7.6	CP-SD-PC/01-2016 - Servicio de Alimentación	16 days	23 Sep '16	17 Oct '16
1374		0%	CP-B-PC/01-201	1.1.4.7.6	CP-B-PC/01-2016 - Material Gastable	16 days	26 Sep '16	18 Oct '16
1378		0%	CP-SD-PC/02-20	1.1.4.7.6	CP-SD-PC/02-2016 - Impresión	16 days	23 Sep '16	17 Oct '16
1382		34%	CD-SD-03/2016	1.1.4.7.7	CD-SD-03/2016 - Diplomado de Formación de	82 days	01 Jul '16	25 Oct '16
1389		26%		1.2	Componente 2: Apoyo a la mejora e integración de las estadísticas laborales e institucionales (USD\$	1346 days	30 Jan '12	29 Mar '17

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1390		34%		1.2.1	Sub-Componente 2.1: Gestión Personal OMLAD y	1268 days	30 Jan '12	08 Dec '16
1391		100%		1.2.1.1	Producto 30: Personal del OMLAD remunerado	1154 days	30 Jan '12	30 Jun '16
1393		100%		1.2.1.2	Producto 31: Nuevo personal del OMLAD incorp	1154 days	30 Jan '12	30 Jun '16
1395		33%		1.2.1.3	Producto 32: Personal del OMLAD capacitado	1268 days	30 Jan '12	08 Dec '16
1396		100%		1.2.1.3.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1397		33%	CD-SD-01/2016	1.2.1.3.2	CD-SD-01/2016 - Diplomado en metodologia d	77 days	23 Aug '16	08 Dec '16
1403		100%		1.2.1.4	Producto 33: Equipos y Materiales de apoyo a la	1178 days	30 Jan '12	03 Aug '16
1404		100%		1.2.1.4.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1405		100%	CP-B-04/2016	1.2.1.4.2	CP-B-04/2016 - Adquisición de material gastab	1 day	03 Aug '16	03 Aug '16
1408		24%		1.2.2	Sub-Componente 2.2: Sistema Integrado de Inform	1282 days	30 Jan '12	28 Dec '16
1409		24%		1.2.2.1	Producto 34: Sistema Integrado de Información Laboral (SIIL) implementado	1282 days	30 Jan '12	28 Dec '16
1410		100%		1.2.2.1.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1411		45%	CCIN-01/2016	1.2.2.1.2	CCIN-01/2016 - Consultoría para el mapeo de l	81 days	01 Jul '16	24 Oct '16
1421		21%	CCIN-03/2016	1.2.2.1.3	CCIN-03/2016 - Consultoría para el mapeo de l	1282 days	30 Jan '12	28 Dec '16
1444		0%	CCIN-04/2016	1.2.2.1.4	CCIN-04/2016 - Diseño de la plataforma integr	97 days	08 Aug '16	21 Dec '16
1467		33%		1.2.3	Sub-Componente 2.3: Estudios del Mercado Labor	1343 days	30 Jan '12	24 Mar '17
1468		33%		1.2.3.1	Producto 35: Estudios del Mercado Labor reali	1343 days	30 Jan '12	24 Mar '17
1469		100%		1.2.3.1.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1470		39%	CCIN-02/2016	1.2.3.1.2	CCI-02/2016 - 5 estudios	241 days	20 Apr '16	24 Mar '17
1471		100%		1.2.3.1.3	Estudios provincias Peravia, La Altagracia y l	186 days	20 Apr '16	05 Jan '17

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1483		100%		1.2.3.1.2	Estudios provincias La Vega y San Pedro de l	100 days	12 May '16	29 Sep '16
1495		0%		1.2.3.1.2	Consultorías en ejecución	125 days	30 Sep '16	24 Mar '17
1508		0%	CP-SD-12/2016	1.2.3.1.3	CP-SD-12/2016 - Publicacion de Estudios	40 days	26 Sep '16	18 Nov '16
1522		31%	CD-SD-05/2016	1.2.3.1.4	CD-SD-05/2016 - Apoyo para investigación uni	162 days	13 May '16	27 Dec '16
1536		0%		1.2.3.1.5	Taller de Capacitación para el Desarrollo de la	44 days	23 Sep '16	24 Nov '16
1537		0%	CCIN-06/2016	1.2.3.1.5	CCIN-06/2016 - Contratación de facilitador	22 days	19 Sep '16	19 Oct '16
1542		0%	CP-SD-PC/01-20	1.2.3.1.5	CP-SD-PC/01-2016 - Servicio de Alimentación	17 days	23 Sep '16	18 Oct '16
1546		0%	CP-SD-05/2016	1.2.3.1.5	CP-SD-05/2016 - Publicación del Plan Nacion	25 days	20 Oct '16	24 Nov '16
1547		0%	CP-SD-05/2016	1.2.3.1.5	CP-SD-05/2016 - Impresión	25 days	20 Oct '16	24 Nov '16
1551		100%		1.2.4	Sub-componente 2.4: Políticas de Empleo	1154 days	30 Jan '12	30 Jun '16
1552		100%		1.2.4.1	Producto 36: Sesiones realizadas de CONAEMPL	1154 days	30 Jan '12	30 Jun '16
1554		100%		1.2.4.2	Producto 37: Mesas de Apoyo Regionales y Sect	1154 days	30 Jan '12	30 Jun '16
1556		100%		1.2.4.3	Producto 38: Talleres Municipales realizados	1154 days	30 Jan '12	30 Jun '16
1558		100%		1.2.4.4	Producto 39: Gastos operativos ejecutados	1154 days	30 Jan '12	30 Jun '16
1560		1%		1.2.5	Sub-Componente 2.5: Sistema Estadístico Instituci	1346 days	30 Jan '12	29 Mar '17
1561		1%		1.2.5.1	Producto 40: Sistema Estadístico Institucional (S	1346 days	30 Jan '12	29 Mar '17
1562		100%		1.2.5.1.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1563		1%	CCIN-01/2015	1.2.5.1.2	CCIN-01/2015 - Consultoría Sistema Estadistic	1346 days	30 Jan '12	29 Mar '17
1583		0%	LPN-B-03/2016	1.2.5.1.3	LPN-B-03/2016 - Adquisición de equipos infor	60 days	25 Nov '16	20 Feb '17
1589		5%		1.3	Componente 3: Monitoreo y Evaluación (USD\$ 932,6	1356 days	30 Jan '12	12 Apr '17
1590		0%		1.3.1	Sub-componente 3.1: Apoyo a la Capacidad de Ge	1324.5 day	30 Jan '12	28 Feb '17

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1591		100%		1.3.1.1	Producto 41: Sistema de Gestión para Empleo di	1154 days	30 Jan '12	30 Jun '16
1593		0%		1.3.1.2	Producto 42: Evaluaciones de procesos y de impacto del SENA realizadas	1324.5 days	30 Jan '12	28 Feb '17
1594		100%		1.3.1.2.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1595		0%	CP-SD-09/2016	1.3.1.2.2	CP-SD-09/2016 - Evento de presentación de ev	61.5 days	02 Dec '16	28 Feb '17
1618		0%		1.3.1.2.3	Evaluación de la Modalidad EIL	71 days	01 Nov '16	08 Feb '17
1619		0%		1.3.1.2.3	Contratación de Digitador	71 days	01 Nov '16	08 Feb '17
1635		0%		1.3.1.2.3	Contratación de Personal para realizar llama	71 days	01 Nov '16	08 Feb '17
1651		100%		1.3.1.3	Producto 43: Evaluaciones de sistemas de monitoreo y de impacto de servicios del	1154 days	30 Jan '12	30 Jun '16
1653		5%		1.3.2	Subcomponente 3.2: Apoyo a la Gestión del Progr	1334 days	30 Jan '12	13 Mar '17
1654		0%		1.3.2.1	Producto 44: Personal de apoyo a la gestión del	1334 days	30 Jan '12	13 Mar '17
1655		100%		1.3.2.1.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1656		0%		1.3.2.1.2	Nómina	180 days	01 Jul '16	13 Mar '17
1657		0%	CCIN-2012-2017	1.3.2.1.2	CCIN-2012-2017 - Gerente Financiero y Adm	180 days	01 Jul '16	13 Mar '17
1668		0%	CCIN-2012-2017	1.3.2.1.2	CCIN-2012-2017 - Encargado de Operaciones	180 days	01 Jul '16	13 Mar '17
1679		0%	CCIN-2012-2017	1.3.2.1.2	CCIN-2012-2017 - Encargado de Supervision	180 days	01 Jul '16	13 Mar '17
1690		0%	CCIN-2012-2017	1.3.2.1.2	CCIN-2012-2017 - Encargado de Evaluación c	180 days	01 Jul '16	13 Mar '17
1701		0%	CCIN-2012-2017	1.3.2.1.2	CCIN-2012-2017 - Chofer Mensajero	180 days	01 Jul '16	13 Mar '17
1712		13%		1.3.2.2	Producto 45: Equipos y material de apoyo a la g	1334 days	30 Jan '12	13 Mar '17
1713		100%		1.3.2.2.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16











Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	






















ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1714		17%		1.3.2.2.7	Otros gastos	1334 days	30 Jan '12	13 Mar '17
1715		22%		1.3.2.2.7	Alquiler de Fotocopiadora (RD\$10,620)	180 days	01 Jul '16	13 Mar '17
1725		22%		1.3.2.2.7	Gastos de Viaticos	180 days	01 Jul '16	13 Mar '17
1735		0%		1.3.2.2.7	Gastos de Notarización	120 days	01 Jul '16	16 Dec '16
1742		0%		1.3.2.2.7	Otros Gastos Operativos	1 day	30 Jan '12	30 Jan '12
1743		0%		1.3.2.2.7	Tarjetas Telefónicas	1 day	30 Jan '12	30 Jan '12
1744		0%	CP-B-03/2016	1.3.2.2.3	CP-B-03/2016 - Aire Acondicionados (1 DGE y 1 DGE)	88 days	01 Jul '16	02 Nov '16
1758		0%	LPN-B-03/2016	1.3.2.2.4	LPN-B-03/2016 - Adquisición de equipos informáticos	45 days	25 Nov '16	30 Jan '17
1764		0%		1.3.2.2.5	Adquisición de material gastable y equipos de oficina	80.5 days	12 Aug '16	05 Dec '16
1765		0%	CP-MO-01/2016	1.3.2.2.5	CP-MO-01/2016 - Adquisición de papel	15 days	12 Aug '16	02 Sep '16
1767		0%	CP-MO-02/2016	1.3.2.2.5	CP-MO-02/2016 - Adquisición de materiales	80.5 days	12 Aug '16	05 Dec '16
1791		0%		1.3.2.2.6	Capacitación en project para equipo de la UEPP	31 days	21 Oct '16	05 Dec '16
1798		50%		1.3.2.2.7	Impresiones y publicaciones	130 days	20 May '16	18 Nov '16
1799		100%	CP-SD-10/2016	1.3.2.2.7	CP-SD-10/2016 - Publicación en periódico Unicef	22 days	20 May '16	20 Jun '16
1804		0%	CP-SD-12/2016	1.3.2.2.7	CP-SD-12/2016 - Publicaciones e impresos varios	40 days	26 Sep '16	18 Nov '16
1818		0%	CP-SD-09/2016	1.3.2.2.8	CP-SD-09/2016 - Evento de Cierre del proyecto	61.5 days	02 Dec '16	28 Feb '17
1841		2%		1.3.3	Subcomponente 3.3: Auditoria	1356 days	30 Jan '12	12 Apr '17
1842		100%		1.3.3.1	Ejecución a junio 2016	1154 days	30 Jan '12	30 Jun '16
1843		0%		1.3.3.2	Pago pendiente Deuda Auditoria de Cierre BID-1601	1154 days	30 Jan '12	30 Jun '16
1844		2%	CD-SD-06/2016	1.3.3.3	CD-SD-06/2016 - Contratación Auditoria	153 days	09 Sep '16	12 Apr '17
1855		0%		2	Hitos del programa	1356 days	30 Jan '12	12 Apr '17

Project: PASNE
Date: 31 Oct '16


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

ID	Task Mo	% Work Complete	Cod. PAC	WBS	Task Name	Duration	Start	Finish
1856	 	100%		2.1	Efectividad legal	1 day	30 Jan '12	30 Jan '12
1857	 	100%		2.2	Elegibilidad	1 day	27 Jun '12	27 Jun '12
1858	 	100%		2.3	Primer desembolso	1 day	27 Jun '12	27 Jun '12
1859	 	0%		2.4	Últmo Desembolso	0 days	30 Jan '17	30 Jan '17
1860	 	0%		2.5	Fin del Programa	0 days	12 Apr '17	12 Apr '17

Project: PASNE
Date: 31 Oct '16





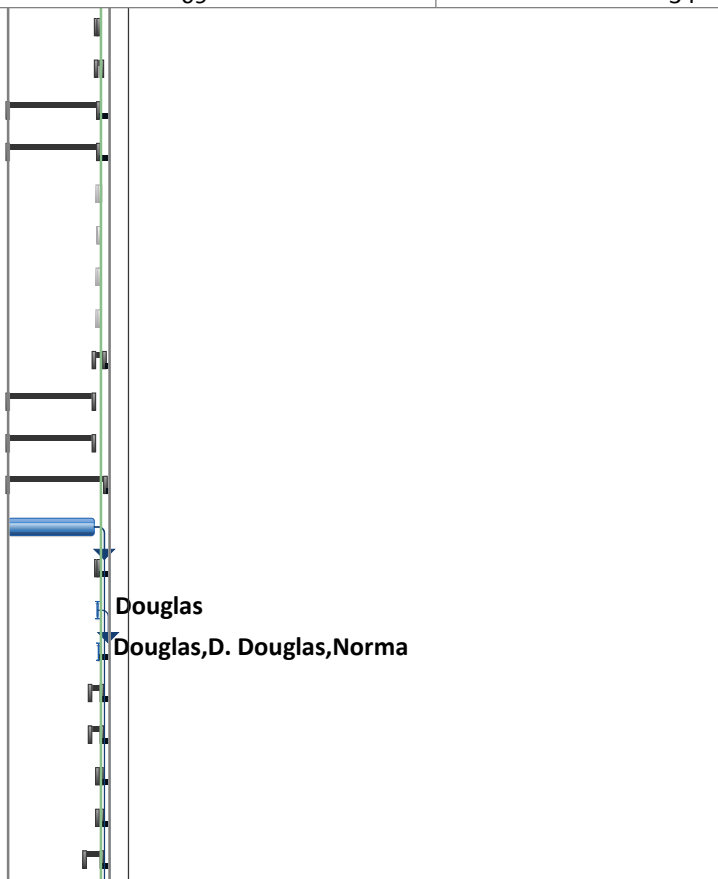
















Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

Predecessor	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84	'09	'34	'34
		CP	EX POST				
	Miosottis	CP	EX POST				
	Miosottis						
		CP	EX POST				
		3CVs	EX POST				
		CP	EX POST				
		CP	EX POST				
		CP	EX POST				
	Miosottis	CD	EX ANTES				
179FS							
	Douglas						
181	Douglas,D. Dougl						
	Miosottis	LPN	EX ANTES				
	Miosottis	CP	EX ANTES				
	Miosottis	CP	EX ANTES				
	Miosottis	CP	EX POST				




Project: PASNE Date: 31 Oct '16	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Slack	

Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	
	Miosottis	CP	EX POST				
	Miosottis	LPN	EX ANTES				
	Miosottis	CP	EX ANTES				
	Miosottis	CP	EX ANTES				
179FS							
	Miosottis	CD	EX ANTES				
	Bienvenido						
	Miosottis						
		CP	EX POST				

Project: PASNE Date: 31 Oct '16	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Slack	

Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	'34
		CP	EX POST				
442	Miosottis	CP	EX ANTES				
	Miosottis	CP	EX POST				
	Miosottis	CP	EX POST				
		CP	EX POST				
		CP	EX POST				

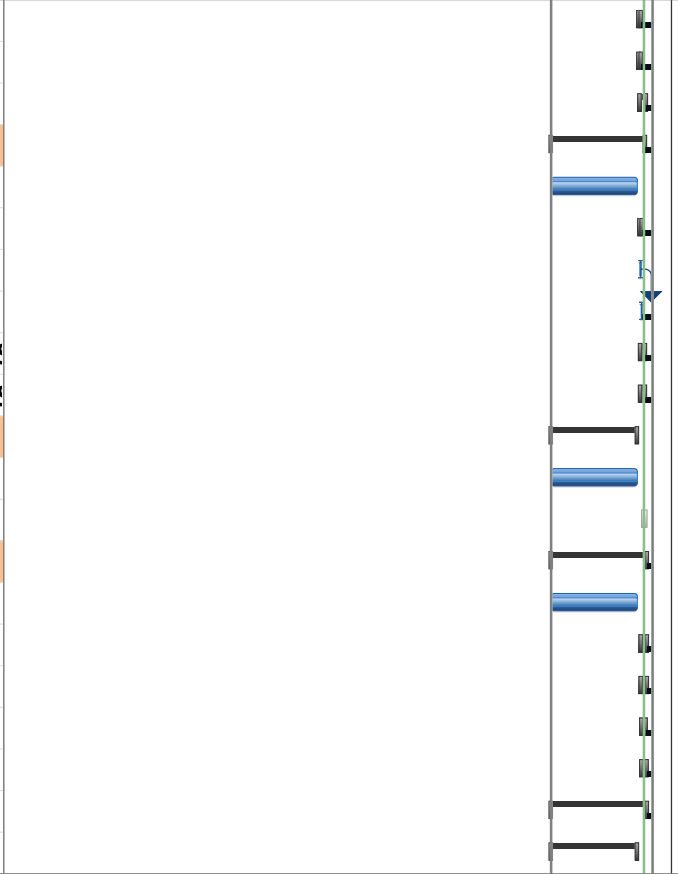


Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	'34
527	Miosottis						
	Miosotlis	CP	EX POST				
		CP	EX POST				
	Miosottis						
		CP	EX ANTES				
		CP	EX POST				
	Douglas	CP	EX ANTES				
	Douglas	CP	EX POST				

Project: PASNE Date: 31 Oct '16	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Slack	

Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84	'09	'34	
653	Norma Douglas	CP	EX ANTES				
	Douglas	SD	EX ANTES				
	Douglas	SD	EX ANTES				
	Douglas		EX ANTES				
1057	Douglas	SD	EX ANTES				
	Douglas						
























Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	
				Douglas			
Douglas			EX ANTES				
Douglas	SD		EX ANTES				
Douglas			EX ANTES				
Douglas	CD		EX ANTES				
			EX ANTES				
	CP		EX ANTES				
	CP		EX ANTES				
	CP		EX ANTES				
	CP		EX POST				
	CP		EX POST				
	CP		EX POST				
Martha González	CD		EX ANTES				

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

Predecessor	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	
	Deyanira	CD	EX ANTES				
		CP	EX ANTES				
	Deyanira	3CVs	EX ANTES				
	Andrés Valentín	3CVs	EX ANTES				
	Andrés Valentín	3CVs	EX ANTES				
	Deyanira	3CVs	EX ANTES				






















Project: PASNE Date: 31 Oct '16	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Slack	

Predec	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	'34
		CP	EX ANTES				
	Deyanira	CD	EX ANTES				
	Deyanira						
1469F	Deyanira	3CVs	EX POST				
	Deyanira	CP	EX POST				
	Bienvenido	CP	EX POST				
			EX POST				
	Carlos Silie	3CVs	EX ANTES				
	Andrés Valentín	CP	EX ANTES				

Project: PASNE Date: 31 Oct '16	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Slack	






















Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	
		CP	EX ANTES				
		3CVs	EX ANTES				
		3CVs	EX ANTES				
		CD	EX ANTES				
		CD	EX ANTES				
		CD	EX ANTES				
		CD	EX ANTES				
		CD	EX ANTES				

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	





















Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84		'09	'34
1713,	Norma		EX ANTES				
1713,	Norma						
1713,	Norma						
		CP	EX ANTES				
		CP	EX ANTES				
		CP	EX ANTES				
		CP	EX ANTES				
1713F							
		CP					
		CP	EX ANTES				
		CP	EX ANTES				
		CP	EX ANTES				
	Norma	CD	EX ANTES				

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	

Preced	Resource Names	METODO DE ADQUISICION	METODO DE REVISION	1984		2034	
				'84	'09	'34	
1					30/01	12/04	

Project: PASNE
Date: 31 Oct '16

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Slack	
